



public works
& infrastructure

Department:
Public Works and Infrastructure
REPUBLIC OF SOUTH AFRICA

WELISIZWE RURAL BRIDGES PROGRAMME

EASTERN CAPE PROVINCE

PROGRESS REPORT FOR

END OF JANUARY 2025

Prepared By: CPM TEAM
Date: 31 January 2025

CONTENTS

EASTERN CAPE PROVINCE.....	1
EXECUTIVE SUMMARY	3
PROGRAMME AND PROJECT TEAM MEMBERS	6
PUBLIC WORKS & INFRASTRUCTURE	6
DEPARTMENT OF TRANSPORT	6
DEPARTMENT OF DEFENCE	6
PHASE A.....	7
Fourteen (14) completed bridges in the Eastern Cape, 2009/10 – 2016/17 Financial Years (ADHOC)	7
PHASE B – CONSTRUCTION OF NINETEEN (19) BAILEY BRIDGES.....	8
BELOW IS THE PROGRESS TO DATE ON THE IMPLEMENTATION OF PLAN – PHASE B.....	9
PHASE C (BFI) - CONSTRUCTION OF SEVENTEEN (17) BAILEY BRIDGES.....	12
LOCAL MATERIAL SUPPLIERS AND EXPENDITURE.....	21
QUALITY OF WORK	22
PROBLEMS ENCOUNTERED	22
CONCLUSION	22
APPENDIX.....	23

EXECUTIVE SUMMARY

The Department of Public Works & Infrastructure (DPWI) and the Department of Defense & Military Veterans (DOD) has entered an Implementation Protocol to implement the Welisizwe Rural Bridges Programme within the Republic of South Africa. The Department of Public Works and Infrastructure also entered into a Memorandum of Agreement (MOA) with the Department of Transport – EC for funding the implementation of Welisizwe Programme.


The programme is aimed at providing urgent safe access to social amenities and further respond to potential disaster areas and emergency disaster situations. The intervention is done through the construction of Modular Steel Bridges using the technical skills from South Africa National Defense Force, Engineer Formation.


This report serves to provide update on the progress made to date in the roll out of Rural Bridges Intervention Programme in the provinces of Eastern Cape. These bridges were prioritized by the Eastern Cape Department of Transport (ECDoT) for construction in the province.

PHASE A - Fourteen (14) bridges in the Eastern Cape, 2009/10 – 2016/17 Financial Years (ADHOC) and Nine (09) bridges in 2018/19 – 2019/20 Financial Years were completed.

PHASE B (EQUITABLE SHARE) - Currently, Twenty (20) bridges were handed over however, Nineteen (19) Bridges are operational.

PHASE C (BFI) - Has seventeen (17) bridges.Ten (10) bridges have been delivered.

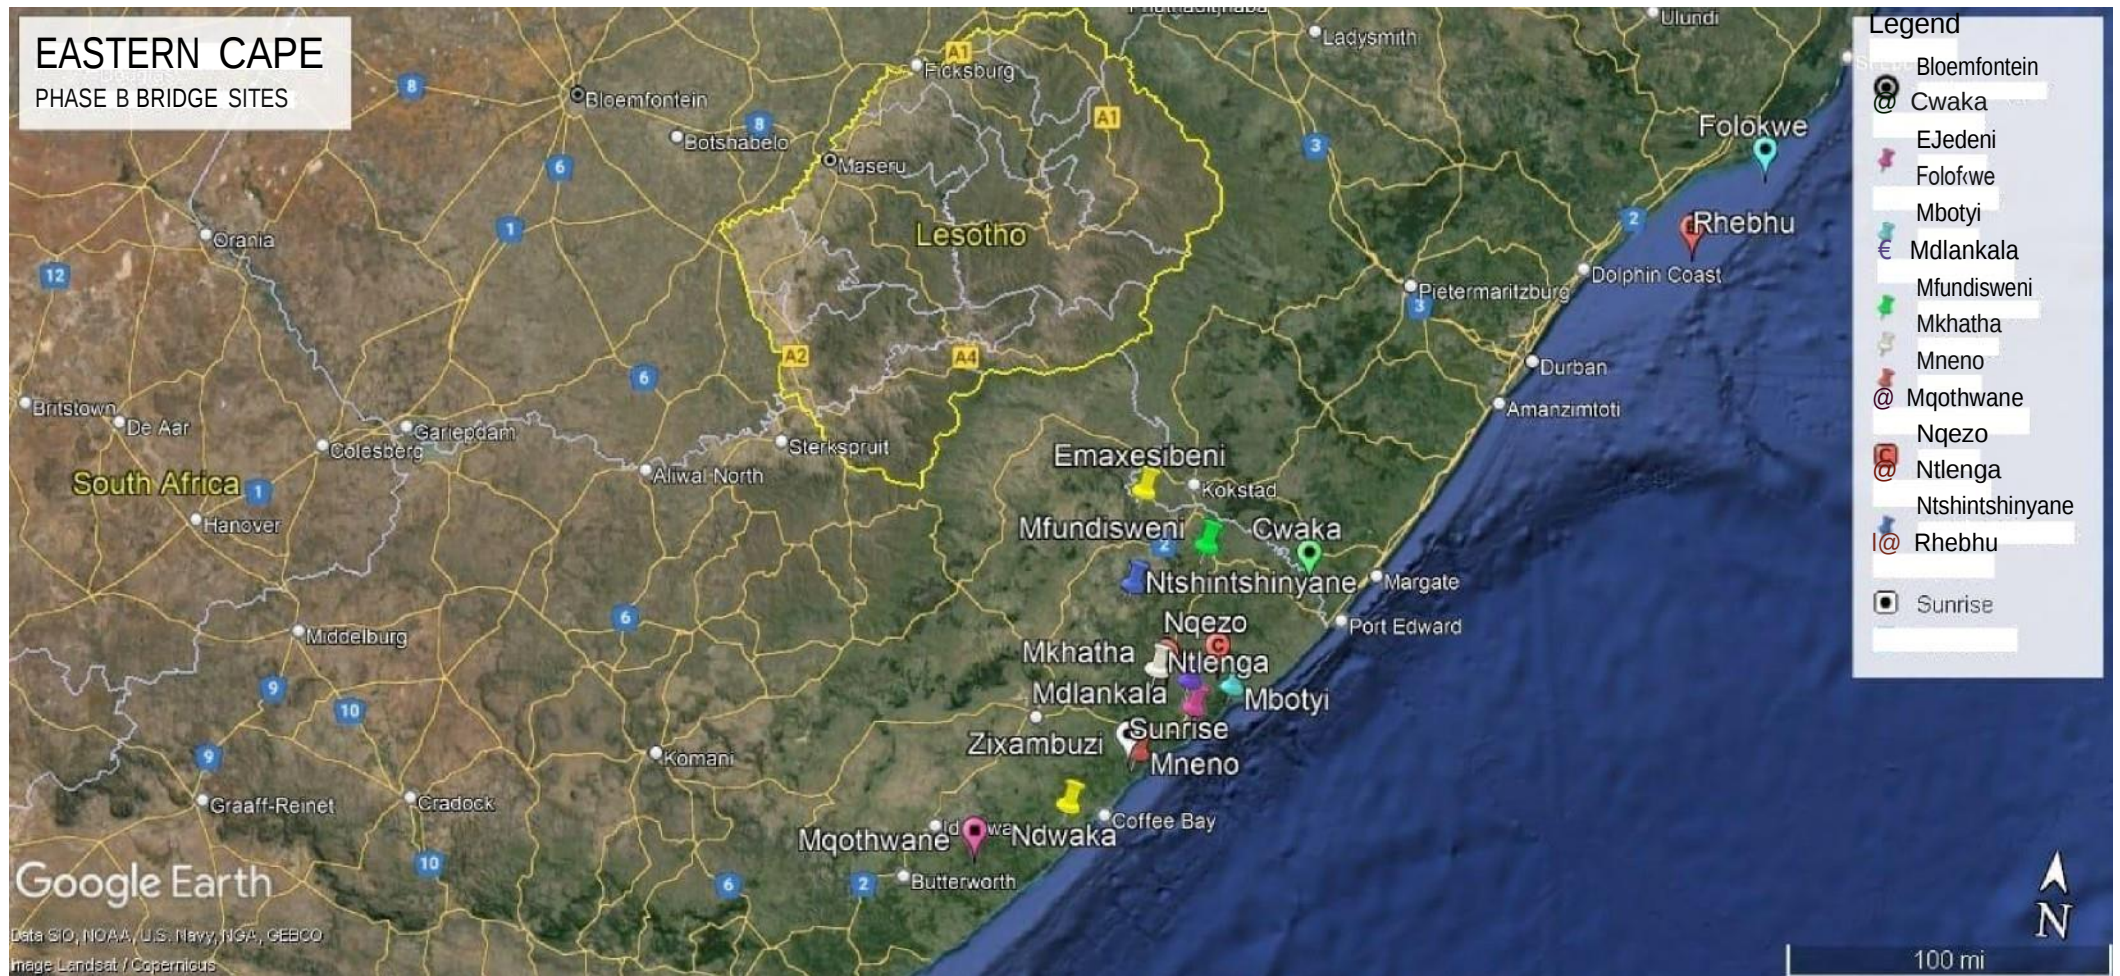

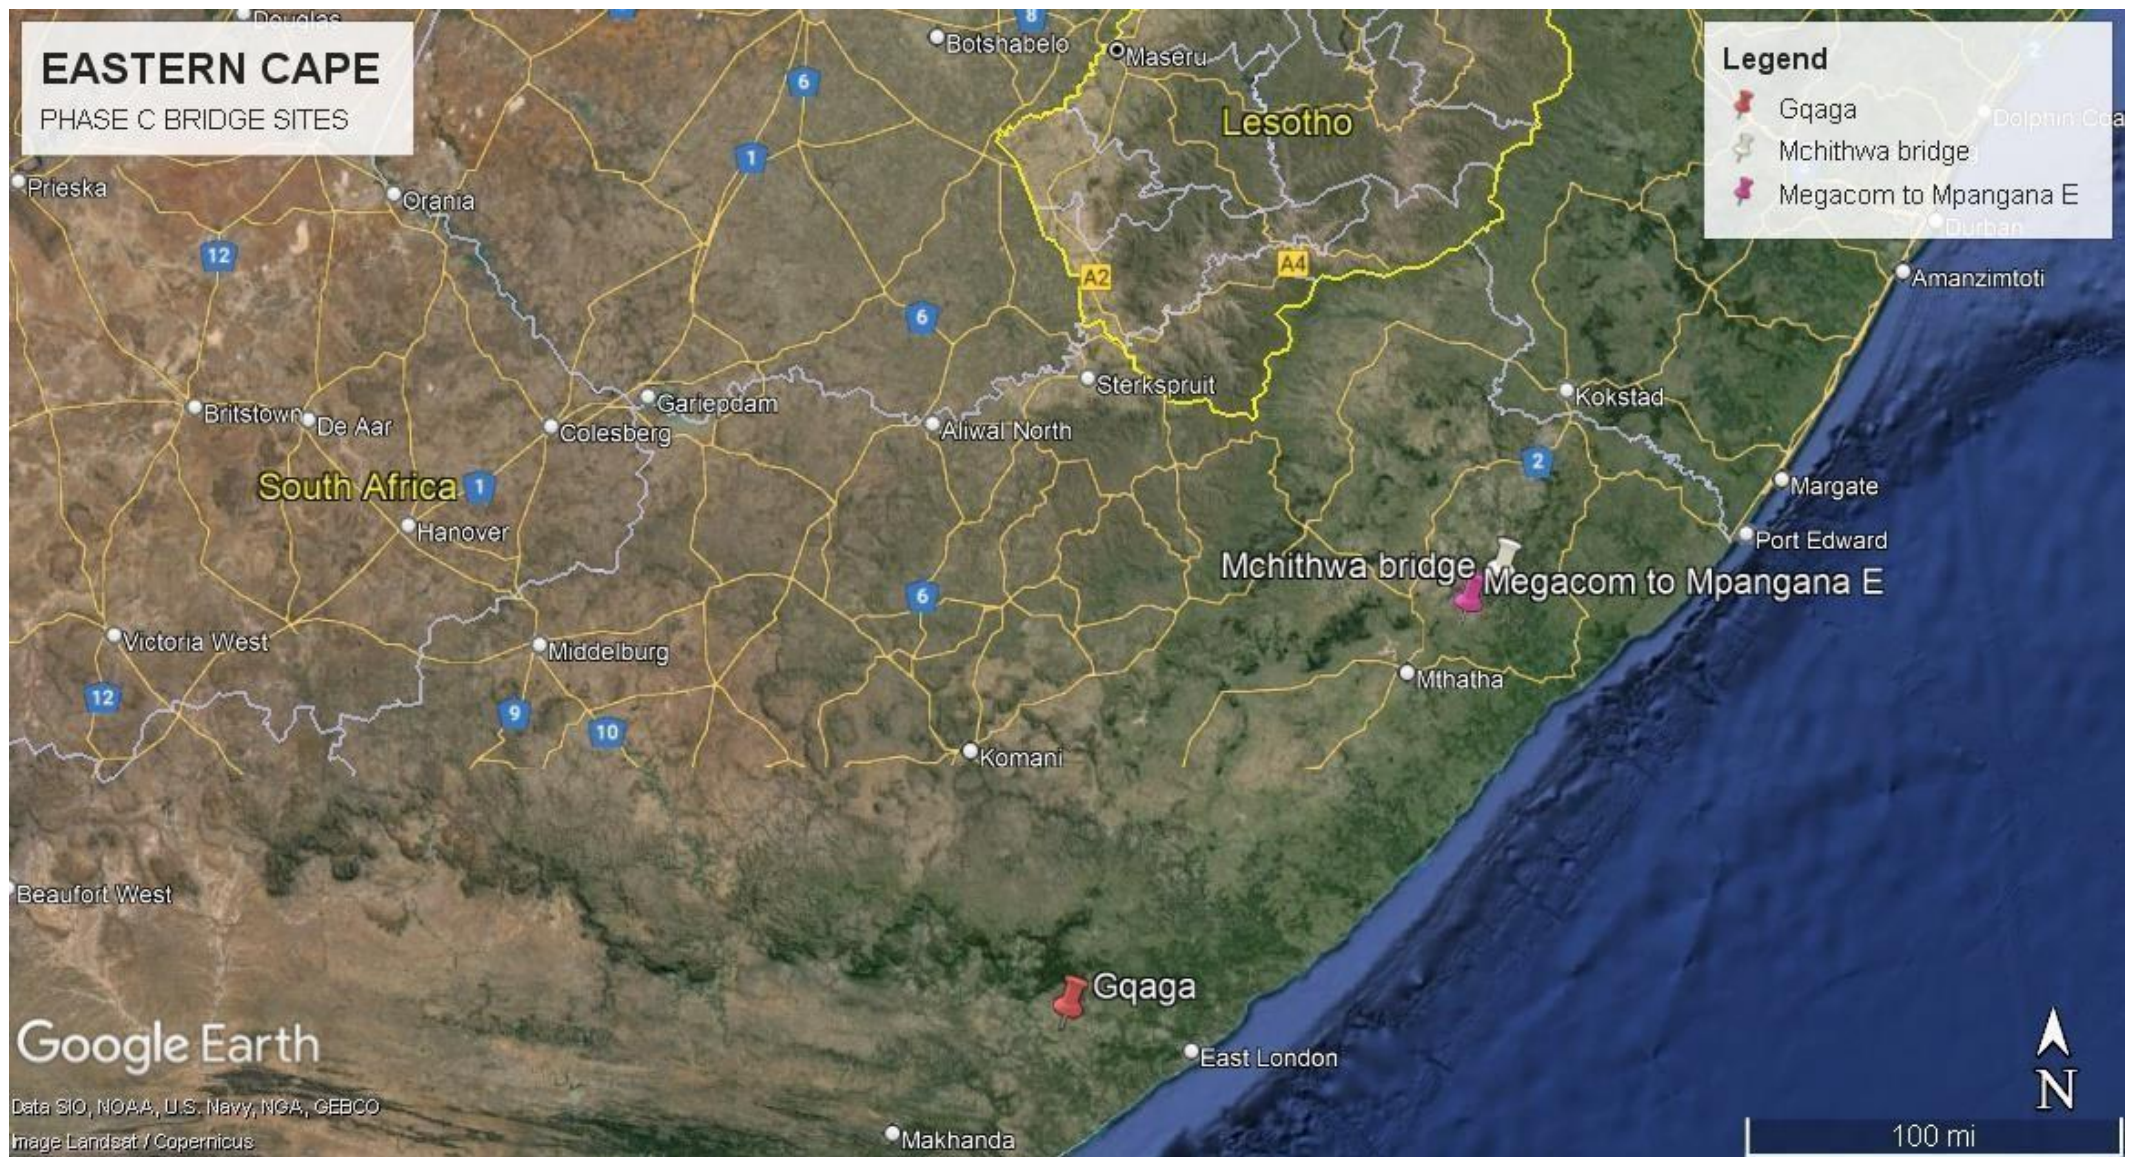

1. PROGRAMME AND PROJECT TEAM MEMBERS

1.1 PUBLIC WORKS & INFRASTRUCTURE

- | | | |
|----|------------------------|------------------------------------|
| 1. | Mr. Stanley Ngobese | Chief Construction Project Manager |
| 2. | Mr. Phumlani Masuku | Programme Coordinator |
| 3. | Ms. Thandekile Ndlovu | Candidate CPM |
| 4. | Ms. Amanda Mamba | Clerk of works |
| 5. | Mr. Siyabonga Ngubo | A/Clerk of Works |
| 6. | Ms. Jabulisile Mathole | Safety Officer Trainee |

1.2 DEPARTMENT OF TRANSPORT

- | | | |
|-----|-------------------------|----------------------|
| 7. | Mr. Clive Boshoff | Chief Civil Engineer |
| 8. | Mr. Thabo Mpalala | Project Manager |
| 9. | Mr. Luvuyo Zonele | EPWP Champion |
| 10. | Ms. Vuyolwethu Ntsaluba | EPWP Champion |
| 11. | Mr. Ayanda Mbulawa | EPWP Champion |

1.3 DEPARTMENT OF DEFENCE

- | | | |
|-----|---------------------|-----------------------|
| 12. | Capt. Z.F. November | Project Officer |
| 13. | Capt. T.W. Malokane | Civil Engineer |
| 14. | Spr G.R. Hendriks | Safety Officer |
| 15. | Capt November | Project officer |
| 16. | Capt Chaka | Project officer |
| 17. | Capt Makamba | Project officer |
| 18. | Major Njingana | Project officer |
| 19. | Capt T Mocumi | Project Officer |
| 20. | Major Setlatjile | Chief Project officer |
| 21. | Spr S Ndlovu | Civil Engineer |

2. PHASE A

I. Eastern Cape consists of twenty-three (23) completed bridges. The list of these completed bridges is provided in the tables below:

II. Fourteen (14) completed bridges in the Eastern Cape, 2009/10 – 2016/17 Financial Years (ADHOC)

NO	BRIDGE NAME	DISTRICT	MUNICIPALITY	BRIDGE TYPE	% PROGRESS
1	Lefukufuku Bridge	Chris Hani	Intsika Yethu Local Municipality	Vehicular	100%
2	Ntafufu Bridge	Alfred Nzo	Port St Johns Local Municipality	Vehicular	100%
3	Daluhlanga Bridge	Alfred Nzo	Mzimvubu Local Municipality	Vehicular	100%
4	Nququ Bridge	Chris Hani	Intsika Yethu Local Municipality	Vehicular	100%
5	Hammanskraal Suspension Bridge	Tshwane Metro	Tshwane Metro	Vehicular	100%
6	Cezu Bridge	O.R. Tambo District	King Sabata Dalindyebo	Vehicular	100%
7	Macoza Bridge	O.R. Tambo District	King Sabata Dalindyebo	Vehicular	100%
8	Mazizi	Alfred Nzo	Mnquma Local Municipality	Vehicular	100%
9	Bawa	Alfred Nzo	Mnquma Local Municipality	Vehicular	100%
10	Popo Bridge Gap 1	Joe Gqabi District	Ulundilini Local Municipality	Pedestrian	100%
11	Popo Bridge Gap 2	Joe Gqabi District	Ulundilini Local Municipality	Pedestrian	100%
12	Popo Bridge Gap 3	Joe Gqabi District	Ulundilini Local Municipality	Pedestrian	100%
13	Popo Bridge Gap 3	Joe Gqabi District	Ulundilini Local Municipality	Pedestrian	100%
14	Ngqunu Bridge	O.R. Tambo District	Mhlontlo Local Municipality	Vehicular	100%

Nine (09) completed bridges in the Eastern Cape 2018/19 – 2019/20 Financial Years.

NO	BRIDGE NAME	DISTRICT	MUNICIPALITY	BRIDGE TYPE	START DATE	COMPLETION DATE	% PROGRESS
1	Nyosana	O.R. Tambo District	Port St Johns	Vehicular	03/10/2018	21/12/2018	100%
2	Queens Mercy	Alfred Nzo	Matatiele	Vehicular	07/01/2019	15/03/2019	100%
3	Zazulwana	Amathole	Mnquma	Vehicular	16/03/2019	12/04/2019	100%
4	Tora	Chris Hani	Engcobo	Vehicular	20/05/2019	10/08/2019	100%
5	Nkobongo	Chris Hani	Engcobo	Vehicular	23/09/2019	20/12/2019	100%
6	Bilatye	Chris Hani	Intshika Yethu	Vehicular	20/01/2020	17/12/2019	100%
7	Fini	Chris Hani	Enoch Mgijima	Vehicular	15/05/2020	28/08/2020	100%
8	Jozana	Joe Gqabi	Senqu	Vehicular	31/08/2020	30/11/2020	100%
9	Ndofela	Joe Gqabi	Senqu	Vehicular	12/01/2021	30/04/2021	100%

- iii. **Practical** completion certificates and final completion certificates to be provided by SANDF.

PHASE B – CONSTRUCTION OF NINETEEN (19) BAILEY BRIDGES

- iv. On 23 March 2023 an amount of R307 886 887, 90 was transferred to DPWI by ECDOT for the implementation of Nineteen (19) Bailey bridges in the 2022/23 Financial Year. Currently, Twelve (12) bridges are boomed are on their final completion stage, and their completion was anticipated by 19 April 2024 but it later revised to be completed by 31 October 2024 if the outstanding material is delivered as scheduled.
- v. The technical assessments were conducted by SANDF between the 15 March 2022 and 21 March 2022.

3. BELOW IS THE PROGRESS TO DATE ON THE IMPLEMENTATION OF PLAN – PHASE B

NO	BRIDGE NAME	BRIDGE TYPE	PLANNED SHO DATE	ACTUAL SHO DATE	PLANNED START DATE	ACTUAL COMPLETION DATE	ANTICIPATED COMPLETION DATE	PROGRESS ON STEEL BRIDGE PROCUREMENT	% WORK PROGRESS
1	EMAXASIBENI Gap 1	Vehicular	08/01/2024	12/01/2024	15/01/2024	19/04/2024	N/A	100 %	0%
2	NTSINTSINYANE	Vehicular	08/01/2024	12/01/2024	15/01/2024	19/04/2024	30/09/2024	100 %	95%
3	MFUNDISWENI	Vehicular	08/01/2024	12/01/2024	15/01/2024	19/04/2024	30/09/2024	100 %	94%
4	MBOTYI	Vehicular	08/01/2024	12/01/2024	15/01/2024	19/04/2024	30/09/2024	100 %	100%
5	DEDENI	Vehicular	08/01/2024	12/01/2024	15/01/2024	19/04/2024	30/09/2024	100 %	100%
6	MDLANKALA	Vehicular	10/05/2023	10/05/2023	23/11/2023	21/02/2024	30/08/2024	100 %	100%
7	MNENO	Vehicular	08/01/2024	12/01/2024	15/01/2024	19/04/2024	30/09/2024	100 %	94%
8	MKHATA	Vehicular	10/05/2023	10/05/2023	23/11/2023	29/02/2024	30/09/2024	100 %	100%
9	NTLENGA	Vehicular	10/05/2023	10/05/2023	19/05/2023	10/11/2023	30/04/2024	100 %	100%
10	RHEBHU	Vehicular	08/01/2024	12/01/2024	15/01/2024	19/04/2024	30/09/2024	100 %	96%
11	DAMBENI	Vehicular	08/01/2024	12/01/2024	15/01/2024	19/04/2024	30/09/2024	100 %	100%
12	CWAKA	Vehicular	08/01/2024	12/01/2024	15/01/2024	19/04/2024	30/09/2024	100 %	100%
13	SUNRISE	Vehicular	10/05/2023	10/05/2023	18/05/2023	10/11/2023	30/04/2024	100 %	100%
14	MQOTHWANE	Vehicular	08/01/2024	12/01/2024	15/01/2024	19/04/2024	30/09/2024	100 %	95%
15	ZIXAMBUZI	Vehicular	08/01/2024	12/01/2024	15/01/2024	19/04/2024	30/09/2024	100 %	100%
16	MDWAKA	Vehicular	08/01/2024	12/01/2024	15/01/2024	19/04/2024	30/09/2024	100 %	69%
17	FOLOKWE	Vehicular	08/01/2024	12/01/2024	15/01/2024	19/04/2024	30/09/2024	100 %	65%
18	MNQEZU GAP 1	Pedestrian	08/01/2024	12/01/2024	02/05/2024	19/04/2024	30/09/2024	100 %	73%
19	MNQEZU GAP 2	Pedestrian	08/01/2024	12/01/2024	13/06/2024	19/04/2024	30/09/2024	100 %	56%
20	WELAKABILI TO SIHLAHLENI	Vehicular	08/01/2024	12/01/2024	15/01/2024	19/04/2024	30/09/2024	100 %	70%

4. COORDINATES FOR ALL BRIDGES UNDER IMPLEMENTATION PLAN- PHASE B

NO	NAME OF THE SITE	BRIDGE TYPE	BRIDGE SPAN	DISTRICT MUNICIPALITY	LOCAL MUNICIPALITY	COORDINATES	WARD NO
1	EMAXESIBENI	Vehicular	36	Alfred Nzo District Municipality	Umzimvubu	30°38'31.78" S 29°12'55.65" E	Ward 6
2	NTSINTSINYANE	Vehicular	30	Alfred Nzo District Municipality	Ntabankulu	31°4'48.358" S 29°11'2.910" E	Ward 3
3	MFUNDISWENI	Vehicular	30	Alfred Nzo District Municipality	Ntabankulu	30°52'46.673" S 29°31'41.761" E	Ward 31
4	MBOTYI	Vehicular	36	O.R.Tambo District Municipality	Ingquza hill	30°38'31.78" S 29°43'45.914" E	Ward 23
5	DEDENI	Vehicular	30	O.R.Tambo District Municipality	Port st johns	31°34'35.540" S 29°32'56.632" E	Ward 10
6	MDLANKALA	Vehicular	36	O.R.Tambo District Municipality	Port st johns	31°27'44.389" S 29°30'53.221" E	Ward 15
7	MNENO	Vehicular	36	O.R.Tambo District Municipality	Port st johns	31°47'9.175" S 29°17'35.787" E	Ward 01
8	MKHATHA	Vehicular	24	O.R.Tambo District Municipality	Port st johns	31°25'38.355" S 29°20'51.473" E	Ward 17/19
9	NTLENGA	Vehicular	24	O.R.Tambo District Municipality	Port st johns	31°24'17.477" S 29°25'27.735" E	Ward 17/19
10	RHEBHU	Vehicular	36	O.R.Tambo District Municipality	Port st johns	31°47'26.788" S 29°20'27.79" E	Ward 01
11	DAMBENI	Vehicular	24	Alfred Nzo District Municipality	Ntabankulu	31° 6'11.02"S, 29°23'32.83"E	Ward 8
12	CWAKA	Vehicular	27	Alfred Nzo District Municipality	Winnie madikizela	30°55'0.068" S 30°4'42.188" E	Ward 21
13	MDWAKA	Vehicular	27	Amathole District Municipality	Mbashe	32°2'31.34" S 28°58'33.55" E	Ward 18
14	SUNRISE	Vehicular	36	Amathole Municipality	Port st johns	31°20'23.817" S 29°27'28.096" E	Ward 20
15	ZIXAMBUZI	Vehicular	30	O.R.Tambo District Municipality	Port st johns	31°52'31.317" S 29°7'53.462" E	Ward 01
16	FOLOKWE	Vehicular	30	Amathole District Municipality	Mbashe	32°05'10.1" S 28°54'45.9" E	Ward 28
17	MQOTHWANE	Vehicular	24	Amathole Municipality	Mbashe	32°14'36.022" S 28°33'21.597" E	Ward 25
18	MNQEZU GAP1	Pedestrian	30	O.R.Tambo District Municipality	Ports st johns	31°24'52.7"S, 29°25'21.0"E	Ward 13
19	MNQEZU GAP2	Pedestrian	30	O.R.Tambo District Municipality	Ports st johns	31°24'53.65"S, 29°25'16.83"E	Ward 13
20	WELAKABILI TO SIHLAHLENI	Vehicular	45	Alfred Nzo District Municipality	Umzimvubu	30°38'31.78" S 29°12'55.65" E	Ward 6

5. END OF APRIL 2024 EXPENDITURE REPORT (PHASE B)

NO	BRIDGE NAME	COST ESTIMATE AS PER DPWI	AMOUNTS PAID TO DATE (EXPENDITURE)	AMOUNT OUSTANDING AS PER REVISED COST
1	EMAXASIBENI GAP 1	15,641,024.09	10,155,820.31	5,485,203.78
2	NTSINTSINYANE	13,990,462.25	8,218,207.59	5,772,254.66
3	MFUNDISWENI SCHOOL	13,990,462.25	8,218,207.59	5,772,254.66
4	MBOTYI	15,641,023.91	10,139,004.00	5,502,019.91
5	DEDENI	14,736,450.02	8,919,035.74	5,817,414.28
6	MDLANKALA	15,641,023.91	10,501,994.03	5,139,029.88
7	MNENO	15,371,254.41	9,651,882.53	5,719,371.88
8	MKHATA 2 ALTERNATIVE	13,855,576.95	11,190,499.36	2,665,077.59
9	NTLENGA	14,731,322.73	12,817,252.87	1,914,069.86
10	RHEBHU	15,641,023.91	10,155,820.31	5,485,203.60
11	DAMBENI	13,855,576.95	8,218,207.59	5,637,369.36
12	CWAKA	15,524,839.71	9,649,264.67	5,875,575.04
13	SUNRISE BRIDGE PSJ	15,641,023.91	14,802,667.04	838,356.87
14	MQOTHWANE	12,098,966.05	6,759,933.69	5,339,032.36
15	ZIXAMBUZI	13,990,462.25	8,218,207.59	5,772,254.66
16	NDWAKA	15,524,839.71	10,139,005.61	5,385,834.10
17	FOLOKWE	14,267,082.11	10,139,005.61	4,128,076.50
18	MNQEZU GAP 1	7,244,923.55	4,220,364.06	3,024,559.49
19	WELAKABILI TO SIHLAHLENI	28,167,282.31	-	28,167,282.31
20	MNQEZU GAP 2	8,362,514.20	4,948,220.53	3,414,293.67
TOTAL		293,917,135.18	177,062,600.72	116,854,534.46

Provincial Allocation	307,886,887.90	177,062,600.72	130,824,287.18
------------------------------	-----------------------	-----------------------	-----------------------

Amount outstanding from cost estimate **116,854,534.46**

Amount outstanding from allocated budget **130,824,287.18**

PHASE C (BFI) - CONSTRUCTION OF SEVENTEEN (17) BAILEY BRIDGES

- vi. During the month of Sept 2023, SANDF conducted technical assessments for fourteen (14) bridges (BFI) funded and only twelve (12) bridges were feasible.
- vii. The cost estimates for one (01) bridge which is Emaxasibeni Gap 2 was submitted to ECDOT and no response was received.
- viii. Eight (8) bridge sites namely Gqaga, Mamfengwini-Busile, Ntushuntushu, Emapoliseni-Mahlubini, Mchithwa, Thomas river, Tsitsa and Megacom to Mpangana SANDF have established the sites and material and bridge components are in a process to be delivered.

ix. BELOW IS THE LIST OF BRIDGE SITES THAT WERE ASSESSED:

NO	BRIDGE NAME	BRIDGE TYPE	SPAN	BRIDGE STATUS	REMARKS
1.	THOMAS RIVER BRIDGE	Vehicular	33	Delivered	10 bridges are in preparation in terms of procurement.
2.	QAGA 1 BRIDGE	Vehicular	24	Delivered	
3.	QAGA 2 BRIDGE	Vehicular	24	Delivered	
4.	MAGQOBHOKENI BRIDGE	Vehicular	30	Delivered	
5.	POTSDAM/ NHLABATHI BRIDGE	Vehicular	36	Delivered	
6.	BALFOUR BRIDGE	Vehicular	36	Delivered	
7.	TINANA BRIDGE	Vehicular	36	Delivered	
8.	TSITSA(KOHLOPONG) BRIDGE	Vehicular	30	Delivered	
9.	NGINGWENI-MTINGWEVU BRDGE	Vehicular	36	Delivered	
10.	ZINQUTU OLWENI LIXENI BRIDGE	Vehicular	36	Delivered	
11.	NCITWA BRIDGE	Vehicular	24	Not Delivered	Bridges have been assessed and components are yet to be procured if funding is provided.
12.	MAMFENGWENI	Vehicular	24	Not Delivered	
13.	NQUBELA	Vehicular	36	Not Delivered	
14.	MEGACOM TO MPANGANA BRIDGE	Vehicular	24	Not Delivered	
15.	SILVERVALE BRIDGE	Vehicular	24	Not Delivered	
16.	EGXENI	Vehicular	36	Not Delivered	
17.	EMAPOLISENI	Feasible but not recommended			

6. END OF MARCH 2024 EXPENDITURE (PHASE C)

NO	BRIDGE NAME	COST ESTIMATE AS PER DPWI	AMOUNTS PAID TO DATE (EXPENDITURE)	AMOUNT OUSTANDING FROM COST ESTIMATES AS PER DPWI
1	THOMAS RIVER BRIDGE	14,599,814.14	8,865,070.62	5,734,743.52
2	QAGA 1 BRIDGE	12,150,638.73	6,718,560.10	5,432,078.63
3	QAGA 2 BRIDGE	12,150,638.73	6,717,848.92	5,432,789.81
4	MAGQOBHOKENI BRIDGE	13,772,543.63	8,167,753.69	5,604,789.94
5	POTSDAM/NHLABATHI BRIDGE	15,438,393.09	9,583,204.66	5,855,188.43
6	BALFOUR BRIDGE	15,438,393.09	9,583,204.57	5,855,188.52
7	TINANA BRIDGE	15,438,393.09	9,583,204.57	5,855,188.52
8	TSITSA (KOHLOPONG) BRIDGE	13,772,543.63	8,168,614.15	5,603,929.48
9	NGINGWENI-MTINGWEVU BRIDGE	15,438,393.09	9,583,204.57	5,855,188.52
10	ZINQUTU OLWENI	15,438,393.09	9,583,204.57	5,855,188.52
	TOTAL	143,638,144.27	86,553,870.42	57,084,273.85
	Provincial Allocation	137,500,000.00	86,553,870.42	50,946,129.58

Amount outstanding from cost estimates - **57,084,273.85**

Amount outstanding from allocated budget - **50, 946 129.58**

7.COORDINATES FOR ALL BRIDGES UNDER IMPLEMENTATION PLAN – PHASE C

NO	NAME OF THE SITE	BRIDGE TYPE	BRIDGE SPAN	DISTRICT MUNICIPALITY	LOCAL MUNICIPALITY	COORDINATES	WARD NO
1	BALFOUR	vehicular	36	Amathole district	Port st johns	32°46'58.63" S 27°29'36.26" E	Ward 9
2	POTDAM/NTHLABATHI	vehicular	36	Amathole district	Raymond Mhlaba	32°58'15.59" S 27°38'33.51" E	Ward 49
3	THOMAS RIVER	vehicular	11	Amathole district	Buffalo City	32°27'14.75" S 27°11'47..16" E	Ward 5
4	ELUPHONDWENI	vehicular	42	Amathole district	Ntabankulu	32°47'24.38" S 27°22'9.55" E	Ward 35
5	ZINGHUTU OLWENI LIXENI	vehicular	36	Chris Hani District	Buffalo City	31°43'51.73" S 27°33'34.12" E	Ward 8
6	QAGA	vehicular	24	Amathole district	Engcobo	34°34'15.564" S 28°13'20.460" E	Ward 6
7	NGINGWENI-MTINGWEVU	vehicular	36	Chris Hani District	Engcobo	34°44'27.024" S 27°35'38.37" E	Ward 8
8	EMAPOLISENI (MAHLUBINI)	vehicular	24	O.R Tambo District	Sakhisizwe	31°26'39.91" S 28°48'24.01" E	Ward 4
9	TINANA	vehicular	36	Joe Gqabi district	Nyandeni	30°34'05" S 28°26'59" E	Ward 11
10	TSITSA	vehicular	30	Joe Gqabi District	Elundini	31°48,25" S 29°29'17.41" E	Ward 7
11	MCHITWA BRIDGE	vehicular	24	OR Tambo District	Nyandeni	31°13.94" S 29°16'34.42" E	Ward 2
12	MAMFENGWENI-BUSILE	vehicular	24	OR Tambo District	AB Xuma	30°37'36.19" S 28°01'50.57" E	Ward 13
13	NQUBELA	vehicular	36	OR Tambo District	Sakhisizwe	31°32'40" S 28°48'59.20" E	
14	MEGACOM TO MPANGANA BRIDGE	vehicular	24	OR Tambo District	Nyandeni	31°50.71' S 29°02'05.84" E	Ward 4
15	SILVERVALE BRIDGE	vehicular	24	Amathole District	Buffalo City	33°53.32" S 27°37'32.97" E	
16	EGXENI	vehicular	36	Alfred Nzo District	Ntabankulu	30°7'13.35" S 29°14'57.47" E	Ward 12
17	EMAPOLISENI	vehicular	24	OR Tambo District	Mhlontlo	31°26'38" S 28°48'25" E	Ward 4

8. LIST OF VARIATION ORDERS

- 8.1 Currently we have two (2) variation orders which belongs to Sunrise and Mnqezu, and we are awaiting for the approval from ECDOT.

9. EXTENTION OF TIME CLAIMS

- 9.1 Request for extension of time was submitted and has been approved. The completion of the bridges is now extended up to 31 January 2024.

10. ENVIRONMENTAL MANAGEMENT AND WATER USE LICENSE

- 10.1 The Environmental officers from DPWI are always in attendance of progress site meetings and site
- 10.2 Approval for exemption in terms of the Environmental Impact Assessment and Water use license was obtained by DPWI from the Department of Fisheries, Forestry & Environmental Affairs and Water and Sanitation.

11. SKILLS DEVELOPMENT

- 11.1 Programme is also contributing towards the skills development initiative as graduates have been appointed such as the Clerk of Works, Artisans, Environmentalist, Quantity Surveyor and Special workman Trainees. 15 DPWI workmen's trainees enrolled for SAMTRAC OHS course that started from 28 October- 1 November 2024.

DESIGNATION	TOTAL NUMBER
Clerk of Works	Seven (7)
Artisans	Eighty – two (82)
Environmental Management Trainee	Two (2)
Special Workman Trainee	Thirty (30)
Quantity Surveying Trainee	Two (1)
Health and safety trainee	One (1)
Project administrator	One (1)
Total	Hundred and thirty four (124)

12. EASTERN CAPE WELISIZWE RURAL BRIDGES PARTICIPANTS PER BRIDGE

NO	SURNAME	FULL NAMES	GENDER	DISABILITY	MOBILE NUMBER	FIELD	DISTRICT MUNICIPALITY	LOCAL MUNICIPALITY	LOCATED BRIDGE SITE
1	Nomlomo	Luyanda	Male	None	0738386377	Carpentry Artisan	Alfred Nzo	Winnie Madikizela	Cwaka
2	Mdunyelwa	Yongama	Male	None	0727464860	Bricklaying Artisan	Alfred Nzo	Winnie Madikizela	Cwaka
3	Bongeka	Mdiya	Female	None	0833114864	Painting Artisan	Alfred Nzo	Winnie Madikizela	Cwaka
4	Mzamo	Msawenkosi	Male	None	0733608968	Painting Artisan	Alfred Nzo	Winnie Madikizela	Cwaka
5	Mvunyiswa	Lindiwe	Female	None	0678478459	Carpentry Artisan	Alfred Nzo	Winnie Madikizela	Cwaka
6	Libazi	Abongile	Male	None	0785603802	Bricklaying Artisan	Alfred Nzo	Winnie Madikizela	Cwaka
7	Mchitwa	Nomangesi	Female	None	0603142476	Civil trainee	Alfred Nzo	Winnie Madikizela	Cwaka
8	Yaliwe	Bawinile	male	None	0782346358	Building trainee	Alfred Nzo	Winnie Madikizela	Cwaka
9	Makaula	Avumile	Male	None	0795348153	Carpentry Artisan	Alfred Nzo	Ntabankulu	Ntsintsinyane
10	Dikiso	Khanya	Female	None	0739970238	Bricklaying Artisan	Alfred Nzo	Ntabankulu	Ntsintsinyane
11	Nqweniso	Zizipho	Female	None	0787248514	Painting Artisan	Alfred Nzo	Ntabankulu	Ntsintsinyane
12	Nqandolo	Mkanyiseli	male	None	0606072594	Carpentry Artisan	Alfred Nzo	Ntabankulu	Ntsintsinyane
13	Fana	Zizipo	Female	None	0624156551	Civil Trainee	Alfred Nzo	Ntabankulu	Ntsintsinyane
14	Ngqondoyi	Anelisa Ssignoria	female	None	0631726436/0813555570	Civil trainee	Alfred Nzo	Ntabankulu	Ntsintsinyane
15	Mlonyeni	Noluvuyiso	Female	None	0839600175	Painting Artisan	Amathole	Mbashe	Mqothwane
16	Makwenke	Aphelele	Male	None	0788872228	Bricklaying Artisan	Amathole	Mbashe	Mqothwane
17	Matinise	Yolanda	Female	None	0786238597	Civil Trainee	Amathole	Mbashe	Mqothwane
18	Ngxuthu	Yondela	Male	Yes	0836743749/0717137360	Carpentry Artisan	Amathole	Mbashe	Mqothwane
19	Matoti	Yolisa	Female	None	0676524274/0839440320	Carpentry Artisan	Amathole	Mbashe	Mqothwane
20	Hina	Viwe	Female	None	0742709861	Painting Artisan	Amathole	Mbashe	Mqothwane
21	Ncalo	Siyanda	female	None	'0781638006	Civil trainee	Amathole	Mbashe	Mqothwane
22	Mazibongo	Sonwabile	Male	None	0710213327	Bricklaying Artisan	Amathole	Mbashe	Folokwe
24	Mzola	Thando	Male	None	0641274975	Welding Artisan	Amathole	Mbashe	Folokwe
25	Gidi	Uzuzole	Female	None	0663439792	Painting Artisan	Amathole	Mbashe	Folokwe
26	Mqatu	Sibusile	female	None	0783146635	Carpentry Artisan	Amathole	Mbashe	Folokwe
27	Mpofu	Luyanda Tamara	Female	None	0734898453	Painting Artisan	Amathole	Mbashe	Folokwe
28	Gangathela	Xolani	Male	None	0737464715	Carpentry Artisan	Amathole	Mbashe	Folokwe

29	Lumkwana	Tandiswa	female	None	0649120616	Civil Trainee	Amathole	Mbashe	Folokwe
30	Makrwanana	Yonela	Female	None	0631677629	Civil trainee	Amathole	Mbashe	Folokwe
31	Xhanko	Bolekwa	Female	None	0734027375	Carpentry Artisan	Alfred Nzo	Ntabankulu	Mfundisweni
32	Harmans	Nokwanele	Female	None	0738417261	Bricklaying Artisan	Alfred Nzo	Ntabankulu	Mfundisweni
33	Kente	Ndiviwe	Male	None	0762477111	Welding Artisan	Alfred Nzo	Ntabankulu	Mfundisweni
34	Ngamlana	Monica	Female	None	0782311516	Painting Artisan	Alfred Nzo	Ntabankulu	Mfundisweni
35	Tywalana	Nosiviwe	female	None	0789312544	Carpentry Artisan	Alfred Nzo	Ntabankulu	Mfundisweni
36	Mzantsi	Sisamnkele	male	None		Civil trainee	Alfred Nzo	Ntabankulu	Mfundisweni
37	Mpeta	Sandisile	Male	None	0834256925	Carpentry Artisan	Alfred Nzo	Mzimvubu	Maxesibeni
38	Mthinti	Siphokazi sheilla	Female	None	0835300398	Civil Trainee	Alfred Nzo	Mzimvubu	Maxesibeni
39	Qokela	Ntobeko	Male	None	0603390239	Carpentry Artisan	Alfred Nzo	Mzimvubu	Maxesibeni
40	Nelani	Masande	Male	None	0792991763	Bricklaying Artisan	Alfred Nzo	Mzimvubu	Maxesibeni
41	Matola	Zimbini Yolanda	Female	None	0739700115	Bricklaying Artisan	Alfred Nzo	Mzimvubu	Maxesibeni
42	Sidlayiya	Okuhle	Female	None	0603720990	Carpentry Artisan	Alfred Nzo	Mzimvubu	Maxesibeni
43	Madulini	Isithandile	Female	None	0798370543	Carpentry Artisan	Alfred Nzo	Mzimvubu	Maxesibeni
44	Dlamini	Lisakhanya	Male	None	0813110433/0828383439	Welding Artisan	Alfred Nzo	Mzimvubu	Maxesibeni
45	Mxhakaza	Ellen	Female	None	0735017472	Painting Artisan	Alfred Nzo	Mzimvubu	Maxesibeni
46	Lokoza	Vuyiseka	female	None	0731267290	Enviro trainee	Alfred Nzo	Mzimvubu	Maxesibeni
47	Makamba	Phozisa	female	None	0691114810	Civil trainee	Alfred Nzo	Mzimvubu	Maxesibeni
48	Daniel	Ntombizodwa	Female	None	0781122065	Carpentry Artisan	Alfred Nzo	Ntabankulu	Dambeni
49	Matiso	Sandiswa	Female	None	0736147693	Bricklaying Artisan	Alfred Nzo	Ntabankulu	Dambeni
50	Jack	Athenkosi	Male	None	0627463413	Painting Artisan	Alfred Nzo	Ntabankulu	Dambeni
51	Nota	Ntombizile	Female	None	0784466359	Painting Artisan	Alfred Nzo	Ntabankulu	Dambeni
52	Vinjwa	Nosipho	female	None	0715010351	Carpentry Artisan	Alfred Nzo	Ntabankulu	Dambeni
53	Mei	Thanduxolo	Male	None	0639929010	Civil trainee	Alfred Nzo	Ntabankulu	Dambeni
54	Mpongwana	Masamnkele	Male	None	0608305322	Civil trainee	Alfred Nzo	Ntabankulu	Dambeni
55	Singqoto	Noluntu	Female	None	0783468043	Painting Artisan	Amathole	Mbashe	Mdwaka
56	Mgwebi	Momelezi	Male	None	0632064719	Carpentry Artisan	Amathole	Mbashe	Mdwaka
57	Mente	Sinesipho	Male	None	0781690230	Bricklaying Artisan	Amathole	Mbashe	Mdwaka
58	Holwana	Vuyiswa	Female	None	0717048426	Carpentry Artisan	Amathole	Mbashe	Mdwaka
59	Makhubalo	Mfumaneko	Male	None	0728085534	Carpentry Artisan	Amathole	Mbashe	Mdwaka
60	Genu	Nikeziwe	Female	None		Civil trainee	Amathole	Mbashe	Mdwaka
62	Thenjiwe	Valashiya	Female	None	0648585404	Painting Artisan	OR Tambo	PSJ	Mkhatha

63	Ziyanda	Qegwana	Female	None	0730857886	Carpenter Artisan	OR Tambo	PSJ	Mkhatha
64	Zimkhitha	Gila	Female	None	0655068220	Bricklaying Artisan	OR Tambo	PSJ	Mkhatha
65	Bhadikazi	Mabusela	Female	Yes	0729233501	Bricklaying Artisan	OR Tambo	PSJ	Mkhatha
66	Ncedisa	Mxokozeli	Female	None	0631677952	Painting Artisan	OR Tambo	PSJ	Mkhatha
67	Mkhosana	Thabo	Male	None	0710565267	Civil trainee	OR Tambo	PSJ	Mkhatha
68	Mkutu	Onke	Male	None	0839635347	Civil trainee	OR Tambo	PSJ	Mkhatha
69	Sinovuyo	Mntuwaphi	Male	None	0734303594	Bricklaying Artisan	O.R Tambo	PSJ	Mnqezu gap1
70	Anathi	Ncombo	Female	None	0820782582	Carpenter Artisan	O.R Tambo	PSJ	Mnqezu gap1
71	Nontlantla	Mvokwe	Female	None	0737019220	Welder Artisan	O.R Tambo	PSJ	Mnqezu gap1
72	Fikeni	Nonelisa	Female	None	0784040933	Painting Artisan	O.R Tambo	PSJ	Mnqezu gap1
73	Nondabula	Zikhona	Female	None	0781220816	QS Trainee	O.R Tambo	PSJ	Mnqezu gap1
74	Bholilitye	Asanele	Female	None	0631150401	Civil trainee	O.R Tambo	PSJ	Mnqezu gap1
75	Martins	Randall	Male	None	0822946447	Civil trainee	O.R Tambo	PSJ	Mnqezu gap1
76	Nocwele	Lunga Fortune	male	None	0737983220	Carpentry Artisan	O.R Tambo	PSJ	Mnqezu gap 2
77	Dudula	Okuhle	Female	None	0710992406	Civil Trainee	O.R Tambo	PSJ	Mnqezu gap 2
78	Sontundu	Asekho	Female	None	0738982964	Civil trainee	O.R Tambo	PSJ	Mnqezu gap 2
79	Mhlakaza	Chuma	Female	None	0790267657	Bricklaying Artisan	O.R Tambo	PSJ	Mdlankala
80	Fani	Anezwa	Female	None	0783554185	Civil Trainee	O.R Tambo	PSJ	Mdlankala
81	Dinwayo	Olwethu	Female	None	0716471899	Painting Artisan	O.R Tambo	PSJ	Mdlankala
82	Nxokwana	Yamnkela	Male	None	064 0653619	Painting Artisan	O.R Tambo	PSJ	Mdlankala
83	Gqetywa	Nomthunzi	Female	None	0737844624	Carpenter	O.R Tambo	PSJ	Mdlankala
84	Duba	Xabiso	Female	None	0740210268	Environmental Trainee	O.R Tambo	PSJ	Mdlankala
85	Maliwa	Lizo	Male	None	0734454718	Welding Artisan	O.R Tambo	PSJ	Mdlankala
86	Ntlokwana	Okuhle	female	None		Civil trainee	O.R Tambo	PSJ	Mdlankala
87	Tshangana	Siyasanga Kenneth	Male	None	0814724784/07 98017265	Civil trainee	O.R Tambo	PSJ	Mdlankala
88	Makaula	Zikhona Amanda	Female	None	0607150718	Civil Trainee	O.R Tambo	PSJ	Mbotyi
89	Sibonda	Mzwandile	Male	None	0718999586	Bricklaying Artisan	O.R Tambo	PSJ	Mbotyi

90	Bongeka	Mfundisi	Female	None	0735904280	Carpentry Artisan	O.R Tambo	PSJ	Mbotyi
91	Jali	Sophumlela	Male	None	0780406427	Carpentry	O.R Tambo	PSJ	Mbotyi
92	Jama	Zodwa	Female	None	0632617542/067 8649501	Carpentry	O.R Tambo	PSJ	Mbotyi
93	Sofute	Noluthando Caroline	Female	None	0647351890	Painting	O.R Tambo	PSJ	Mbotyi
94	Stwayi	Ncebakazi	Female	None	0632972818	Bricklaying Artisan	O.R Tambo	PSJ	Mneno
95	Wayiza	Masamnekele	Male	None	0839514482	Carpentry Artisan	O.R Tambo	PSJ	Mneno
96	Luvuyo	Nosiphiwo	Female	None	0730326749	Painting Artisan	O.R Tambo	PSJ	Mneno
97	Novukela	Vuyiswa	Female	None	0630955463	Civil trainee	O.R Tambo	PSJ	Mneno
98	Ntsandu	Mbuyelwa Anderson	male	None	078444860078 2052978	Carpentry Artisan	O.R Tambo	PSJ	Mneno
99	Diko	Avuma	Male	None	0785736863	Building trainee	O.R Tambo	PSJ	Mneno
100	Mtshiyi	Thabani Simanye	female	None	'0639706283	Civil trainee	O.R Tambo	PSJ	Mneno
101	Ngqukumba	Ntembeko	Male	None	0735891947	Bricklaying Artisan	O.R Tambo	PSJ	Rhebu
102	Matshisi	Nosipho	female	None	0737632183	Carpentry Artisan	O.R Tambo	PSJ	Rhebu
103	Nzoyiya	Buyisa	Female	None	0738516316	Carpentry Artisan	O.R Tambo	PSJ	Rhebu
104	Mabindla	Anathi	Female	None	0632358993	Painting Artisan	O.R Tambo	PSJ	Rhebu
106	Xolo	Yamkela	female	None	0789212327	Civil trainee	O.R Tambo	PSJ	Rhebu
107	Magobodi	Andiswa	female	None	0727436797	Bricklaying Artisan	O.R Tambo	PSJ	Zixambuzi
108	Makapela	Mzwethemba	male	None	0632754946	Carpentry Artisan	O.R Tambo	PSJ	Zixambuzi
109	Qinga	Zimkita	female	None	0633560953	Carpentry Artisan	O.R Tambo	PSJ	Zixambuzi
110	Makanda	Zimasa	female	None	0782739141	Painting Artisan	O.R Tambo	PSJ	Zixambuzi
111	Mjacu	Zezethu	female	None	0632384283	Civil trainee	O.R Tambo	PSJ	Zixambuzi
112	Ngxishe	Mkhonzeni	male	None	0685708174	Civil trainee	O.R Tambo	PSJ	Zixambuzi
113	Mhlahlo	Nolundi	Female	None	0664598486/07 35084522	Project Admin	O.R Tambo	MTHATHA	PRD OFFICE
114	Lingani	Babalo	male	None		QS Trainee	O.R Tambo	MTHATHA	PRD OFFICE
115	Sinina	Esethu	Female	None	0833929973	Carpentry Artisan	O.R Tambo	PSJ	Dedeni
116	Twenani	Kanyisa	Female	None	0639387891	Painting Artisan	O.R Tambo	PSJ	Dedeni
117	Soni	Samkelisiwe	Female	None	0788236063	Civil Trainee	O.R Tambo	PSJ	Dedeni
118	Mpaka	Bukhobenkosi	Male	None	0630743337/07	Bricklaying Artisan	O.R Tambo	PSJ	Dedeni

					91956915				
119	Ntlali	Siziphiwe Noncedisa	female	None	0785687225	Carpentry Artisan	O.R Tambo	PSJ	Dedeni
120	Maquthu	Ntombokuqala	female	None	0782428879	Painting Artisan	O.R Tambo	PSJ	Dedeni
121	Gana	Amanda Inga	female	None	0761473894	Civil trainee	O.R Tambo	PSJ	Dedeni
122	Mpeta	Sandisile	Male	None	0834256925	Carpentry Artisan	Alfred Nzo	Umzimvubu	eMaxesibeni
123	Mthinti	Siphokazi sheilla	Female	None	0835300398	Civil Trainee	Alfred Nzo	Umzimvubu	eMaxesibeni
124	Qokela	Ntobeko	Male	None	0603390239	Carpentry Artisan	Alfred Nzo	Umzimvubu	eMaxesibeni
125	Nxusani	Nobubele	Female	None	0634111356	Civil Trainee	Alfred Nzo	Umzimvubu	Mfundisweni

13. EASTERN CAPE WELISIZWE RURAL BRIDGES CLERK OF WORKS PER BRIDGE SITE

NO	SURNAME	FULL NAMES	GENDER	DISABILITY	MOBILE NUMBER	FIELD	DISTRICT MUNICIPALITY	LOCAL MUNICIPALITY	LOCATED BRIDGE SITE
1.	Namhla	Sokapase	Female	No	0625290054	Clerk of Works	Alfred Nzo	Winnie Madikizela	Cwaka
2.	Mamba	Amanda	Female	No	0833446247	Clerk of Works	Amathole	Mbashe	Mqothwane
3.	Ntombizodidi	Mtshizana	Female	No	0733602938	Clerk of Works	Alfred Nzo	Mzimvubu	Maxesibeni
4.	Thandolwethu	Mama	Male	None	839441362	Clerk of Works	Amathole	Mbashe	Mdwaka
5.	Onke	Ntongana	Male	None	0734016998	Clerk of works	OR Tambo	PSJ	Ntlenga
6.	Maqa	Luyanda	Male	None	0655851500	Clerk of works	O.R Tambo	PSJ	Dedeni
7.	Tiba	Mtiya	Male	none	0723459604	Clerk of works	O.R Tambo	PSJ	Sunrise

NB: There are currently 37 DPWI employees who are not on site because their contracts ended on January 16, 2025, and others whose contracts ended on January 31, 2025. The department has directed that there will be no contract renewals, but new contracts will be issued as soon as the submission is received from head office.

14. LABOUR REPORT

14.1 ECDOT is responsible for the recruitment of EPWP.

14.2 EPWP participants has been recruited from the community and a total number of 40 workers will be involved in each bridge site as detailed below:

NO	BRIDGE NAME	BRIDGE TYPE	PLANNED	ACTUAL	STATUS
1	Ntlenga	Vehicular	40	0	Completed
2	Sunrise	Vehicular	40	0	Completed
3	Mkhata	Vehicular	40	0	Complete
4	Mdlankala	Vehicular	40	0	Completed
5	Rhebhu	Vehicular	40	0	Semi-complete
6	Dambeni	Vehicular	40	0	Completed
7	Cwaka	Vehicular	40	0	Complete
8	Ndwaka	Vehicular	40	36	Under Construction
9	Zixambuzi	Vehicular	40	0	Complete
10	Mqhothwane	Vehicular	40	36	Under construction
11	Emaxasibeni Gap 1	Vehicular	40	0	Not yet started
12	Welakabili to Sihlahleni	Vehicular	40	40	Under construction
13	Ntsintsinyane	Vehicular	40	46	Semi-complete
14	Mfundisweni	Vehicular	40	40	Semi-complete
15	Mbotyi	Vehicular	40	0	Semi-complete
16	Dedeni	Vehicular	40	0	Semi-complete
17	Mneni	Vehicular	40	0	Damaged by floods
18	Folokwe	Vehicular	40	36	Under construction
19	Mnqezu gap 1	Pedestrian	40	40	Under construction
20	Mnqezu gap 2	Pedestrian	40	40	Under construction

15. LOCAL MATERIAL SUPPLIERS AND EXPENDITURE

15.1 As part of SMMEs development the local suppliers have been appointed by BSE to deliver the raw materials for construction materials using the local municipality's database. The list of all other suppliers will be provided in the next report.

NO	BRIDGE NAME	SUPPLIER NAME	PRODUCT PURCHASED	AMOUNT
1	NTHLENGA	NSINGIZA HOLDINGS	GABION STONES & MATERIALS	1,112,321.40
		GABION BASKETS	BASKETS	733,274.27
		HI TAP	TOOLS, Hardware	106,855.91
		KKOM	STEEL	195,350.00
		TXZ HOLDINGS	GABION STONES & MATERIALS	458,161.15
		SKHOT HOLDINGS	STEEL WIRES	33,166.00
				2,639,128.73
2	SUNRISE	GABION BASKETS	BASKETS	733,274.27
		SKMOT HOLDINGS	GABION STONES	733,436.08
		KKOM GROUP	STEEL	195,350.00
		HITAP	POWER TOOLS	150,349.97
		NSINGIZA HOLDING	GABION STONES & CRUSHER	360,450.00
		MSKN LOGISTIC	READY MIX	127,880.00
				2,300,740.32
3	NDLANKALA	KKOM GROUP	STEEL	130,643.80
		SKHOMT HOLDINGS	GABION STONES & SANDS	477,121.78
		HI TAP	TOOLS	128,936.05
				736,701.63
4	MKHATHA	HITAP	TOOLS	130,643.80
		NSINGIZA HOLDINGS	GABION STONES & SANDS	410,025.00
		KKOM GROUP	STEEL	156,070.00
		GABION BASKETS	BASKETS	44,086.30
				740,825.10

16. QUALITY OF WORK

- 16.1 Quality of work undertaken by SANDF on bridge sites is noticed and appreciated. Site activities are being carried out and monitored as construction progresses.

17. PROBLEMS ENCOUNTERED

Bridge projects have not progressed as planned due various reasons, such as:

- 17.1 Slow pace delivery of material by BT suppliers to the bridge sites, they started delivering on the 29 January 2025 to Mnqezu gap1, Mnqezu gap 2 and at Mneno Bridge.
- 17.2 The Crane Truck was returned to the service provider after breaking down, Mnqezu gap 1, Mnqezu gap 2, and Folokwe still needs their bridge parts delivered however on the 29 January 2025 bridge parts for Folokwe bridge were delivered on site.
- 17.3 The ready-mix concrete supplier for the Mdwaka and Folokwe bridge sites has been appointed, at Folokwe we are preparing to pour concrete for bases and columns on the 07 February 2025
- 17.4 On the 12 January 2025, the Port St Johns region experienced heavy rainfall, resulting in severe flooding. The intense flow of water caused extensive damage to Mneno bridge structure, rendering it unworkable. The damages were observed on concrete ramp walls, the walls of the ramps leading to the bridge suffered significant structural damage, with large sections being swept away and steel bridge frames the main steel components of the Bailey Bridge were dislodged and displaced, ultimately found in the middle of the river.

18. CONCLUSION

- 18.1 In Eastern Cape all 19 bridge sites have been handed over to SANDF for construction.
- 18.2 The implementation of the 17 Bridges has been planned to commence in stages depending on the completion of the 19 Bridges. DOD has established the Eight (8) bridges namely Gqaga, Tsitsa, Thomas river, Mchithwa, Mamfengwini-Busile, Ntushuntushu, Emapoliseni-Mahlubini, and Megacom to Mpangana.
- 18.3 Progress in some bridge sites has increased to 60% completion. The practical completion assessment was conducted from November 26 to 29, 2024, for (10) ten partially completed bridges; however, only (08) eight bridges were declared fit to serve as an emergency crossing for pedestrians and traffic during the rainy days of December; these bridges are Sunrise, Ntlenga, Mdlankala, Mkhatha, Dambeni, Zixambuzi, Mfundisweni, and Mbotyi. The remaining two bridges, Cwaka and Ntsintsinyane, still need to have their approach roads constructed.
- 18.4 Delivery of bridge parts for Gqaga Bridge was done on the 03rd December 2024.
- 18.5 Dr. AB XUMA local municipality has made a request to construct the Lucwecwe Bridge, which will be an extra bridge under the 17 bridge.

19. APPENDIX

- 19.1 Ntlenga
- 19.2 Sunrise
- 19.3 Mkhatha
- 19.4 Mdlankala

- 19.5 Rhebhu
- 19.6 Emaxasibeni Gap 1
- 19.7 Cwaka
- 19.8 Ndwaka
- 19.9 Zixambuzi- Port St Johns
- 19.10 Mqhothwane
- 19.11 Dambeni
- 19.12 Ntsintsinyane
- 19.13 Mfundisweni
- 19.14 Mbotyi
- 19.15 Dedeni
- 19.16 Mneni
- 19.17 Folokwe
- 19.18 Mnqezu gap 1
- 19.19 Mnqezu gap 2
- 19.20 Emaxasibeni Gap 4

PROJECTS ON SITE FOR EASTERN CAPE (PHASE B)



NTLENGA – BEFORE CONSTRUCTION

NTLENGA – DURING CONSTRUCTION



SUNRISE- BEFORE CONSTRUCTION

SUNRISE- DURING CONSTRUCTION



MKHATA – BEFORE CONSTRUCTION

MKHATA – DURING CONSTRUCTION





Mdlankala – BEFORE CONSTRUCTION

Mdlankala – DURING CONSTRUCTION



Mdwaka Before Construction

Mdwaka During construction



Mqothwane Before Construction

Mqothwane | During construction





Ntsintsinyane Before Construction

Ntsintsinyane During construction



Mfundisweni Before Construction

Mfundisweni | During construction



Dambeni Before Construction

Dambeni During construction





Cwaka Before Construction



Mbotyi Before Construction



Rhebu Before Construction

Cwaka during construction



Mbotyi during construction



Rhebu During Construction





Mneno before construction

Mneno during construction



Emaxasibeni before construction

Emaxasibeni during construction



Dedeni before construction

Dedeni during construction






Folokwe before construction

Folokwe during construction



zixambuzi before construction

Zixambuzi during construction

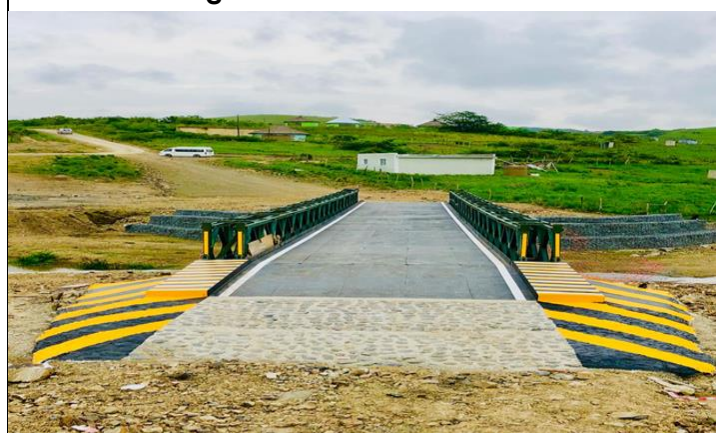

Mnqezu gap1 during construction



Mnqezu gap1 before construction



Mnqezu gap 2 before construction



Mnqezu gap2 during construction

END OF REPORT
